FIRST & FINAL

Orginal/Duplicate/Triplicate

AEE/SSD/BBR 97/15-16 Dt-31-7-15

CONTRACT CERTIFICATE

(For other works)

No.....

Date:.....

Division:

BR NO 266/15-16 30/9/15

Sub-Division:

Bill Received No.....Dated.....Cash Book Vocher No.....Dated.....

Scheduled Doeket No.....

Head of Account.....

Name of work (as Per Sanctioned Estimate.):- **Improvements to Footpath in 2nd Cross road and other roads near Srirama temple in Mallasandra, in Ward No. 13, in Shettyhalli Sub- Division.**

Name of Contractor and Full Address: : - **Sri. B UMESH, No. 127, 3rd Cross, Ramaiah Enclvave, Bangalore-560073.**

Reference to Agreement No: **EE/DD/WO/338/14-15** 25-6-15 27-6-15

Certified that the measurements were taken by me on 31-7-15 and recorded in pages 34.24.08 - 34.24.12

Measurements Book No. 3425/14-15 and that the work is satisfaction executed

Contractor Signature.

Officer-in-charge of work.

Certified that the measurements were taken by me on 25/6/15 & 31/7/2015 and found correct. The work is satisfactorily executed

Certified that the quantities of materials shown in column 3 of Account II have been actually brought to site of the work and the contractor has not previously received any advance on this security. These materials are of an imperishable nature and are all required for immediate use on the work in connection with items for finished work have been agreed upon. A normal agreement signed and executed by the contractor is recorded in the office.

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ಪಶ್ಚಿಮ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಕಛೇರಿ ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು

31/7/2015

If Memorandum of Payment **Work Code No. 013-15-000004**

		Amount
1	Total Value of work done or supplies made as per account.	Bill Amount - 1395406=00
2	Deduct amount to be held in reserve being ..... Percent Rs.	IT - 13954=00
3	Deduct amount to be held in reserve being balance	VAT - 55816=00 (-) 91950=00
4	Deduct payments: a) Amount of previous payment as in the office Cash Book Vocher No..... Dated..... S.D. No..... Amount adjusted towards cash advance recovery of b) Payments cost store or other materials supplied.	LWC - 13954=00 CBF - 1395=00 Total... Roy - 6831=00
5	Balance being unpaid value of work done held in reserve	
6	Deduct cash advance made on the office cash book vehicle No..... Dated..... Less adjustments	
7	Net amount due to or from contractor	Net Amount - 1303456=00
8	Unadjusted items Advance to contractor for materials brought to site (as detailed) within value of Government materials supplied. Government materials supplied.	

Contractor Signature.

Received Rs.....(in wards).....

Audited and admitted for Rs. 1395406=00

By cash and by adjustment of payment as per memorandam.

Payment by Cheque for Rs. 1303456=00

Witnesses:

1 (.....)

2 by adjustment Rs. 91950=00

(fo use in the office)

Date:.....

Paid by me by cheque.....Dated.....

Cash Rs.....Dated:

Accounts Superintendent

Executive Engineer

Signature of Contractor

Initials of Officer making payment dated.....

Executive Engineer.

COMPLETION REPORT

1	Name of the work	Improvements to Footpath in 2nd cross road and other roads near Srirama Temple in Mallasandra, in Ward No. 13, in Shettyhalliub- Division.
2	Sanctioned Estimate No. & Date	CE/D2/AS/55/14-15 dt 29/10/2014
3	Head of Account which is chargeable	Programme of works 14-15 Year- 2014-15
4	~~Instrument~~ Work Order NO. & Date	EE/DO/40/338/14-15 Date-31/3/2015
5	Name Of Contractor	Sri. B UMESH, No. 127, 3rd Cross, Ramaiah Enclvave, Bangalore-560073.
6 a	Time Stipulated for Completion of work	90days
b	Delay in Exculpation of Work	
7	Measurement recorded in	3425/14-15
8	Check Measurement of the Asst	342408-412/1
9	Name of the office/official in charge of the work	Shettyhalli Subdy Dasarahalli division
10	a) Asst. Eng/junior Eng	G. Nagabhushan
	b) Asst. Exe Engineer	B.L Jayalingappa

Sanctioned Estimate Amout	Amout Claims As per Actually Vide As per bills	Excess	Savings
15-00 Lakhs	13,95,406/—	—	Rs. 6478/-

1) Certified that the above work has been completed within the stipulated time noted in the
2) Certified that the contractor has delayed and completed the work for which necessary fine recovered
3) Certified that the above work has been executed by the contractor satisfactory in

ASSISTANT ENGINEER.

ASSIATANT EXECUTIVE ENGINEER

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಸಹಾ.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು

31/8/15
ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ದಾಸರಹಳ್ಳಿ ವಲಯ, ಬೆಂಗಳೂರು

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ದಾಸರಹಳ್ಳಿ ವಲಯ, ಬೆಂಗಳೂರು

ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
Bruhat Bangalore Mahanagara Palike

BBMP ENGINEERING DEPARTMENT

Road History Data Sheet

General

Zone	Ward No.	Ward Name
DASARAHALLI	13	Mallasandra
Street ID	**Street Name**	**Significant Landmark**
W0010, W0017, W0015, W0003, W0005, W0001, W0008, W	NA	SRIRAMA TEMPLE
Segment No.	**Total Length (m)**	
13/C-W0010/S011755	203.41	

Segment Details

Seg No.	Length (m)	Start Coordinates		End Coordinates		From	To
1	73.56	77.510441	13.057733	77.511104	13.057872	I0231	W0005
2	28.95	77.510232	13.058297	77.510497	13.058268	W0015	W0017
3	100.90	77.508492	13.058859	77.509396	13.058644	W0017	I10009

Work Details

History of Road / Lane / Circles

Name of the Work	Sanctioned Estimated Amount (Rs.)	Sanctioned Year
IMPROVEMENTS TO FOOTPATH IN 2ND CROSS ROAD & OTHER ROADS NEAR SRiRAMA TEMPLE	1500000	2014
Year	**Type of Work**	**Other Work Type**
2014 - 2015	Footpath Layering	
Tender	**Work Details**	**Job No. / Work Code**
Tender		013-15-00004
Work Order No.	**Work Order Date**	**Period of Extention**
EE\DD\WO\338\14-15	31/03/2015	
Defect Liability Period From	**Defect Liability Period To**	**Multiple road involved with the same Job No/ Work Code #**
		Yes

Contractor Details

Name of Contractor	Contractor Reg No (BBMP/PWD)	Expenditure Booked \ Released (Rs)
B UMESH		0.00
Phone No.	**E-Mail ID**	
9980485938		

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.

Field Inspection Details

Number of Trees	Any Other Information	Name
0		nagabhushan G
Date of Inspection	**Remarks**	
15/09/2015		

Category	Image	Photo Remark
Footpath Condition		This photo seems out of range
Footpath Condition		This photo seems out of range
Footpath Condition		This photo seems out of range

Remarks

Designation	Approver Name	Date	Target Date	Remark
CE	SIDDEGOWDA	15/09/2015	15/10/2015	
EE	MALATHESHA R	15/09/2015	15/10/2015	
AEE	JAYALINGAPPA BL	15/09/2015	15/10/2015	
AE	NAGABHUSHAN G	15/09/2015	15/10/2015	
AE	NAGABHUSHAN	15/09/2015	15/10/2015	

Zone: DASARAHALLI **Ward No:** 13 **Ward Name:** Mallasandra **Street ID:** W0010, W0017, W0015, W0003, W0005, W

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು

301462

ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

Bruhat Bangalore Mahanagara Palike

ನರಸಿಂಹರಾಜ ಚೌಕ, ಬೆಂಗಳೂರು–560 002.

ಬಿಬಿಎಂಪಿ

ಕಾಮಗಾರಿ ಸಂಖ್ಯೆ ಪ್ರಮಾಣಪತ್ರ

Job Number Certificate

Copy | **Number : 013-15-000004**

Ward	:	013 Mallasandra
Zone	:	Dasarahalli
Division	:	Dasarahalli
Year	:	2015
Estimate	:	1500000.00 (Current Works) Rupees Fifteen Lakhs
POW SL.No	:	
Comm. Approval	:	Para 13 of file / 21-Oct-2014
Nature	:	New
Catagory	:	General Ward(POW) Works
Department	:	Engineering Division
Type	:	Road
Subtype	:	Comperansive Development/Improvement
Budget Head	:	P1771 Zone Works - POW Works

Name of Work :
Improvement to footpath in 2nd cross road and other roads near srirama temple in Mallasandra in ward no. 13 shettyhalli sub division.

EE Details :
User Name : CwDas
Create Date : 25-Oct-2014 17:22:12.625
Remarks :

CW Details :
User Name : AsDasJN
Create Date : 27-Oct-2014 13:12:21.437
Remarks :

Zone Details :
User Name : AsDasJN
Create Date : 27-Oct-2014 13:12:21.593
Remarks :

CAO Details :
User Name : AcfDasJN
Create Date : 27-Oct-2014 15:42:24.687
Remarks :

DDO : ddo030 Executive Engineer Dasarahalli
CE : Parameshwaraiah
EE : Jogisiddegowda

For Bruhat Bangalore Mahanagara Palike

Printed on : 11-Dec-2015 12:24
Print Count : 2

ಸಹಾಯಕ ನಿಯಂತ್ರಕರು (ಹಣಕಾಸು)
Chief Accounts Officer

9455196447670459794551964476704597/9455196447670459794551964476704597/9455196447670459794551964476704597/

Note: This is a computer generated certificate. Any manual alteration / entry will invalidate this document.

Earlier Job Number generated with security number 77732834545895457 for above work stands cancelled due to the corrections made with necessary approvals.

AEE/SSD/SBR97/15-16 BR 266/30-9-15

M. A. R. 57 (Rule 116)

Measurement Book

No. B

Serial No. 1st & Final Bill 31-7-15

Name of Work Improvements to Footpath in 2nd Crossroad & other roads near Srirama temple in Mallasandra, in ward No. 13, in SSD. 342408

Name of Contractor of nature of Agency From To

Date of commencement of work

Date	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	1) WO NO : EE/DD/WO/338/14-15, Date : 31/3/2015						
	2) Job Code Number : 013-15-000004						
	3) A.S NO : CE/D2/AA/055/14-15, Dt : 29/10/2014						
	4) T.S NO : EE/DD/TS/103/14-15, Dt : 29/10/2014						
	5) Tender Notification NO : BBMP/EE/DD/Ten/03/2014-15, Dt : 31/10/2014						
	6) Est Cost Rs. 15.00 Lakhs						
	7) Name of the Contractor : Sri Umesh Date of completion :						30.6.2015
	8) Date of ~~Recording~~ Submission of Bill :	31-7-15				P. Code : 1771	

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
1)	Earthwork excavation by manual means in ordinary soil breaking an average horizontal throw upto 2 metres and an average lift upto 0.5 m, excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods Complete as per specifications with all leads and lifts etc., Complete as per specification & direction of Engineer-in-charge of the work. TMB Page No :- 342483/1 to 342485/2				vide @ Rs.	167.06 Cum 75.60	⇒ 12,630=00
2)	Providing & laying in position plain cement concrete of mix M10 with cement @ 180 kg with 40 mm and down size graded granite metal coarse aggregates @ 0.86 cum & fine aggregates @ 0.58 cum, machine mixed, Concrete laid in layers, not exceeding 15 cm thick well compacted in foundation and plinth including cost of all materials, labour, Hire of machinery, curing etc, complete as per specification and direction of Engineer-in-Charge of the work.						

M. A. R. 57 (Rule 116)
Measurement Book

No. B

342409

Serial No. .....

Name of Work ..... From ..... To .....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	TMB page no :- 342486/1 to 342487/2			Qty	vide @ Rs.	34.96 2486.35	Cum ⇒ 86,923=00
3)	Removing B.S slab of drain & stacking with all leads and lifts etc, Complete as per specification & direction of Engineer in charge of the work. TMB page no :- 342488/1 to 342488/2			Qty	vide @ Rs.	200.32 58.32	Sqm ⇒ 11,682=00
4	Refixing stone slabs of drain & ~~stacking~~ pointing in cm 1:3 with all leads & lifts etc, Complete as per specification and direction of Engineer-in-charge of the work. Qty vide Item no. 3				~~Qty~~ @ Rs.	200.32 75.60	Sqm ⇒ 15,144-00

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
5)	Providing Granite slabs of selected quality roughly dressed and fixed in cement mortar (1:6) including fixing curing etc., Complete as per specification & direction of Engineer-in-charge of the work TMB page no : 342488/2			Qty	vide @ Rs	14.99 639.36	Sqm ⇒ 9,581=00 9584=0
6)	Providing & Constructing precast Concrete solid blocks with Compressive strength not less than 35 kg/sqm with cement mortar 1:4 masonary (Quoin, Jamb, Closer blocks) with solid Concrete blocks of size 40x20x20 cms Confirming to IS : 2185/1965 in superstructure including cost of materials, labour, charges, Scaffolding, curing Complete as per specification and direction of Engineer-in-charge of the work TMB page no : 342489/1 to 342489/2			Qty	vide @ Rs.	207.20 993.60	Sqm ⇒ 2,05,874=00

M. A. R. 57 (Rule 116)
Measurement Book

No. B

342410

Serial No. .....
Name of Work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
7)	Providing and Constructing precast concrete solid blocks with Compressive strength not less than 3.5 mewton per sqm with cement mortar 1:4 masonry (quoin, Jamb, closer blocks) with Solid cement blocks of size 40 x 15 x 20 cms Confirming to I.S : 2185/1965 in superstructure including cost of materials, labour charges, Scaffolding, curing complete as per specifications with all leads and lifts etc, complete as per specification and direction of Engineer - in- charge of the work. TMB page NO : 342490/1 to 342490/2				Qty vide — @ Rs.	207.20 sqm 940.68	sqm ⇒ 1,94,909=00
3)	Providing flush pointing to Square rubble, course or uncoursed Stone masonry with cement mortar 1:3, 20 mm deep after raking joints to depth of 20mm nicely lining, including cost of materials,						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	labour, curing complete as per specification and direction of Engineer-in-charge of the work. TMB Page No :- 34249 1/1 to 34249 2/2			Qty	vide @ Rs.	207.20 sqm 91.80 ⇒	19,021=00
9)	Providing and laying in position plain cement concrete of mix M15 with cement @ 240 kgs, with 20 mm and d/s graded granite metal coarse aggregates @ 0.878 cum and fine aggregates @ 0.459 cum, machine mixed, Concrete laid in layers not exceeding 15 cms, thick well compacted, in foundation, plinth and cills, including cost of materials, labour, Hom of machinery, curing complete as per specification and direction of Engineer-in-charge of the work. TMB Page no :- 34 2492/1 to 34 2492/2			Qty	vide @ Rs.	10.36 Cum 5327.64 ⇒	55,194=

M. A. R. 57 (Rule 116)
Measurement Book

No. B 342411

Serial No. .....

Name of Work ..... From..... To.....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Date	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
10)	Providing & laying reinforced cement ~~pro~~ precast slabs of mix CC 1:1½:3 using 20mm & downsize graded granite metal using HYSD 10mm dia steel @ 100mm c/c both ways & complete as per specification & direction of Engineer-in-charge of the work.						
		1	23.70	0.90		21.33	
		1	22.00	0.90		19.80	
		1	19.30	0.90		17.37	
		1	12.40	0.90		11.16	
		1	28.00	0.90		25.20	
		1	1.50	0.90		1.35	
		1	30.00	0.90		27.00	
		1	30.00	0.90		27.00	

Measurements checked and found correct

A.E. (D&R.)

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Measurements checked & found correct E.E. 3/10/20	1	30.00	0.90		27.00	
		1	2.50	0.90		~~21.97~~ 2.25	
		1	24.40	0.90		21.96	
		1	24.00	0.90		21.60	
	I Cr Rd Syracuse Temple Rd RK	1	30.00	0.90		27.00	
		1	3.00	0.90		2.70	
		1	30.00	0.90		27.00	
		1	3.00	0.90		2.70	
	2nd Cr RK Shelfield Rd	1	16.50	0.90		14.85	
		1	26.50	0.90		23.85	
		1	25.00	0.90		22.50	
		1	7.60	0.90		6.84	
		1	25.00	0.90		22.50	
		1	8.00	0.90		7.20	
		1	10.80	0.90		9.72	
		1	16.70	0.90		15.03	
		1	6.30	0.90		5.67	

M. A. R. 57 (Rule 116)
Measurement Book

No. B

342412

Name of Work ..... From ..... To .....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Item	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4	5	6	7	8
		1	14.00	0.90		12.60	
		1	15.00	0.90		13.50	
	Missed slab -						
	Kurempu school road	27	0.60	0.90		14.58	
	3rd cross road	30	0.60	0.90		16.20	
	Shetty halli main road	28	0.60	0.90		15.12	
						482.58	
	Measurement Checked & Level Unexceptionable						
				Qty limited to	Sch qty	482.40	Sqm
					@ Rs.	1600=00	⇒ 7,71,840=00
11)	Disposal of debris to the final place of disposal with all lead & lift & as direction by the engineer in charge of the work, lead 3 Km a) Basic rate for lavalage of materials, as per Item no. 17.4	KSRRB : M100 - 4.1 :					

E.E. (D.D.)

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Rs. 2.00 Tonne/Km b) Average lead of work 1.28 Tonne/Km for Rs. 2.00/Km c) Add loading & unloading Complete as per Specification and direction of Engineer-in-Charge of the work.						
	Qty vide Item No. 1					167.06 Cum	
						@ Rs. 75.47 ⇒ 12,608=00	
						Bill Amount of Rs.	13,95,406=00
	1) The Contractor has done the work satisfactorily.						
	2) The Contractor has removed the Debris from workspot.						
	ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು ಶಿಕ್ಷಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ ಎಸ್.ಎಂ ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.						31-7-15

M. A. R. 57 (Rule 116)

Measurement Book

No. B

342413

Serial No. .....

Name of Work .....

Name of Contractor or nature of Agency .....

Date of commencement of work .....

Audited and admitted for Rs. 1395406=00 From 1302456=00

by Cheque for Rs. 91950=00

Date	Full description, etc. of work	Dimensions				Contents		Reference to last Measurement
		Number	Length	Breadth	Depth			
1	2	3	4	5	6	7		8

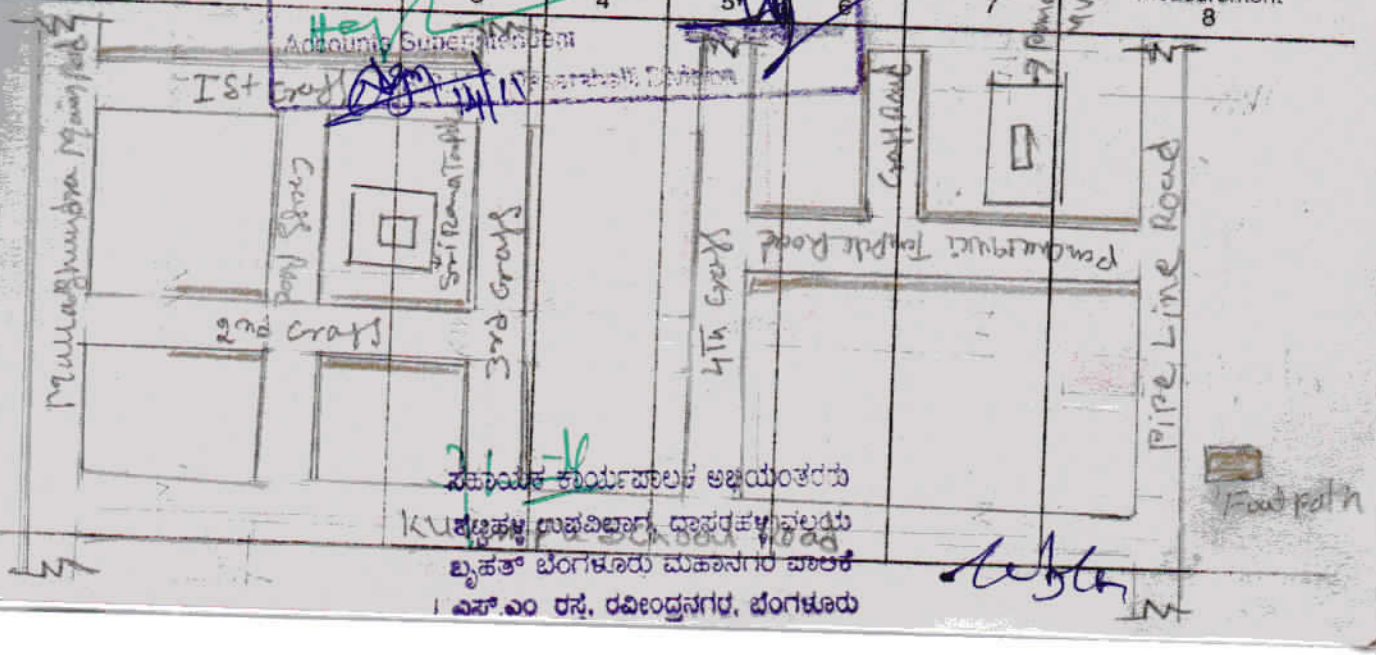

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶಿವಾಜಿನಗರ ಉಪವಿಭಾಗ, ದಾಪರಹಳ್ಳಿವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
1 ಎಸ್.ಎಂ ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು

AEE/BNSK/1st Bill

1st & Final Bill — A3)7-15

M. A. R. 57 (Rule 116)
Measurement Book

BR 265/30-9-15
No. B

342415

Serial No. .....

Name of Work improvements to footpath 8th, 7th crossroads of 3rd main road, in ward no. 13, in SSD From ..... To .....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
1)	Work order NO : EE/DD/WO/339/14-15, Date : 31/3/2015						
2)	Job code NO : 013-15-000009						
3)	AA NO : EE/D2/AA/056/14-15, Date : 29/10/2014						
4)	TS NO : EE/DD/TS/104/14-15, Date : 29/10/2014						
5)	Tender Notification NO & Date : BBMP/EE/DD/Tem/03/14-15, Dt : 31/10/2014						
6)	Name of the Agency : B. Umesh						
7)	Est. Cost Rs. 15.00 Lakhs					Select Completion 31-8-15	
8)	Date of ~~Submission~~ BILL :		31-7-15			P. code : 1771	

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
1)	Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2 meters and an average lift upto 0.5 m, excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications with all leads and lifts etc., complete as per specification & direction of Engineer-in-charge of the work.						
	TMS page no :- 342460/1 to 342461/2			Qty	vide	171.57 cum @ Rs. 75.60 ⇒	12,971-00
2)	Providing & laying in position plain cement Concrete of mix M10 with cement @ 180 kg with 40mm and down size graded granite metal coarse aggregates @ 0.86 cum and fine aggregates @ 0.58 cum, machine mixed, Concrete laid in layers not exceeding 15 cms thick, well compacted in foundation and plinth including cost of all materials, labour, hire of machinery, curing etc complete as per specification and direction of Engineer-in-charge of the work.						

M. A. R. 57 (Rule 116)
Measurement Book

No. B

342416

Serial No. .....

Name of Work ..... From ..... To .....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Sl. No. 1	Full description, etc. of work 2	Dimensions: Number 3	Length 4	Breadth 5	Depth 6	Contents 7	Reference to last Measurement 8
	TMB page no :- 342462/1 to 342463/1			Qty	vide @ Rs.	35.91 2548.80	Cum ⇒ 91,527=00
3	Removing D.S slab of drain & stacking with all leads and lifts etc., complete as per specification & direction of Engineer-in-charge of the work						
	TMB page no :- 342463/1 to 342463/2			Qty	vide @ Rs.	198.90 58.32	Sqm ⇒ 11,600=00
4	Refixing Stone slabs of drains & pointing in CM 1:3 with all leads & lifts etc., Complete as per specification and direction of Engineer-in-charge of the works						
	~~TMB page no :-~~	Qty vide Item no. (3)			@ Rs.	198.90 75.60	Sqm ⇒ 15,037=00

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
5)	Providing Granite slabs of selected quality roughly dressed and fixed in cement mortar (1:6) including fixing curing etc., Complete as per specification and direction of Engineer-in-charge of the work. TMS page No :- 342464/1				Qty vide @ Rs.	6.40 sqm 639.36 ⇒ 4,092=00	
6)	Providing & Constructing precast concrete solid blocks with Compressive strength not less than 35 kg/sqm with cement mortar 1:4 masonry (quoin, Jamb, closer blocks) with solid concrete blocks of size 40 x 20 x 20 cms confirming to IS 2185/1965 in superstructure including cost of materials, labour charges, scaffolding, curing complete as per specification and direction of Engineer-in-charge of the work. TMS page No :- 342464/1 to 342464/2				Qty vide @ Rs.	212.80 sqm 993.60 ⇒ 2,11,438=00	

M. A. R. 57 (Rule 116)
Measurement Book

No. B

342417

Name of Work ..... From ..... To .....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
	2	Number 3	Length 4	Breadth 5	Depth 6	7	8
4	Providing and constructing precast concrete solid blocks with compressive streangth not less than 3.5 newton per sqm with cement motor 1:4 masonry (quion, Jamb, closer blocks) with solid concrete blocks of size 40 x 15 x 20 cms, confirming to IS 2185/ 1965 in superstructure including cost of materials, labour charges, scaffolding, curing complete as per specifications with all leads and lifts etc., complete as per specification & direction of Engineer-in-charge of the work.						
	TMB page NO : 342465/1 to 342465/2			Qty	vide @ Rs	212.80 sqm 940.68	sqm ⇒ 2,00,177=00
5	Providing flush pointing to square rubble, course or uncoarsed stone masonry with cement motar 1:3, 20 mm deep, after raking						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	joints to depth of 20 mm, nicely lining, including cost of materials, labour, curing complete as per specification and direction of Engineer-in-charge of the work.						
	TMB page no :- 3424 65/2 to 3424 66/1			Qty	vide @ Rs.	212.80 91.80	Sqm ⇒ 19,535=00
9)	Providing & laying in position plain cement Concrete of mix M15 with cement @ 240 Kgs, with 20 mm & downsize graded granite metal coarse aggregate @ 0.878 cum and fine aggregate @ 0.459 cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick well compacted, in foundation, plinth & cills, including cost of all materials, labour, Hom of machinery, curing complete as per specification and direction of Engineer-in-charge of the work.						
	TMB page no :- 3424 66/2 to 3424 67/1			Qty	vide @ Rs.	10.64 5327.64	Cum ⇒ 56,686=00

M. A. R. 57 (Rule 116)
Measurement Book

No. B

342418

Serial No. .....

Name of Work ..... From ..... To .....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Date	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
18/	Providing & laying reinforced cement precast slabs of mix cc 1:1½:3 using 20 mm & d/s graded granite metal using HYSD 10mm dia steel @ 100 mm c/c both ways & completeas per application & direction of Engineer-in-charge of the works.						
	3rd cross, From 4th main to 3rd main R/S	1	27.00	0.90		24.30	
		1	26.70	0.90		24.03	
		1	30.00	0.90		27.00	
		1	30.00	0.90		27.00	
		1	30.00	0.90		27.00	
		1	28.00	0.90		25.20	
		1	13.50	0.90		12.15	
		1	24.00	0.90		21.60	
		1	24.00	0.90		21.60	

Measurements Checked & found correct

E.E. (D.D.)

ಕಾಮಗಾರಿಯ ಅಳತೆಗಳು ಸರಿಯಾಗಿವೆ.

ಕಾರ್ಯಪಾಲಕ ಎಂಜಿನಿಯರ್ (ಪ್ರ.ದ.)

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Measurements checked & found correct	1	30.00	0.90		27.00	
		1	3.50	0.90		3.15	
		1	12.00	0.90		10.80	
		1	22.00	0.90		19.80	
		1	25.20	0.90		22.68	
		1	30.00	0.90		27.00	
	7th cross, 3rd main, main R/S	1	30.00	0.90		27.00	
		1	30.00	0.90		27.00	
		1	30.00	0.90		27.00	
		1	12.00	0.90		10.80	
		1	30.00	0.90		27.00	
		1	21.70	0.90		19.53	
	mixed slabs — 8th cross 2nd main	25	0.60	0.90		13.50	
		12	0.60	0.90		6.48	
						478.62	
			Qty limited to	sch Qty		478.62 sqm	
					@ Rs.	1600=00	⇒ 7,65,792=

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

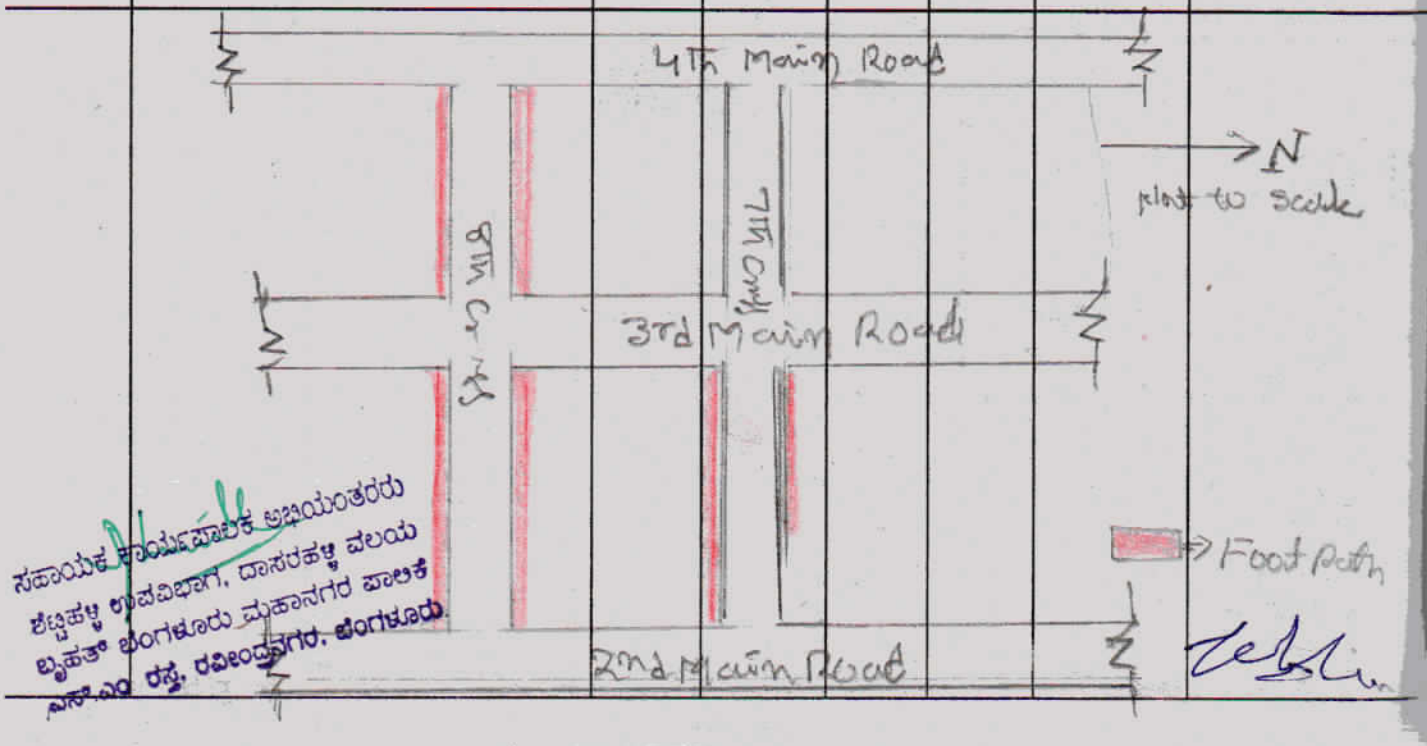

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.

COMPLETION REPORT

1	Name of the work	Improvements to Footpath 8th, 7th cross roads of 3rd main road, in ward no 13 in Shettyhalli Sub-Division.
2	Sanctioned Estimate No. & Date	CE/D2/AS/~~SE~~/14-15 dt 29/10/2014
3	Head of Account which is chargeable	Programmed works year 2014-15
4	Instrument Order NO. & Date	GE/DD/20/339/14-15 Date-31-3-2015
5	Name Of Contractor	Sri. B UMESH, No. 127, 3rd Cross, Ramaiah Enclvave, Bangalore-560073.
6 a	Time Stipulated for Completion of work	90 days
b	Delay in Exculpation of Work	
7	Measurement recorded in	3425/14-15
8	Check Measurement of the Asst	342575 to 419
9	Name of the office/official in charge of the work	Shettyhalli sub division Dasarahalli division
10	a) Asst. Eng/junior Eng	G. Nagu bhargem
	b) Asst. Exe Engineer	B.L. Jayalingappa

Sanctioned Estimate Amout	Amout Claims As per Actually Vide As per bills	Excess	Savings
15.00 Lacks	14,01,803/-	—	Rs 288/-

1) Certified that the above work has been completed within the stipulated time noted in the
2) Certified that the contractor has delayed and completed the work for which necessary fine recovered
3) Certified that the above work has been executed by the contractor satisfactory in

ASSISTANT ENGINEER.

31/8/15
ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ದಾಸರಹಳ್ಳಿ ವಲಯ, ಬೆಂಗಳೂರು

ASSISTANT EXECUTIVE ENGINEER

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು

ಮುಖ್ಯ ಅಭಿಯಂತರರು
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
Bruhat Bangalore Mahanagara Palike

BBMP ENGINEERING DEPARTMENT

Road History Data Sheet

General

Zone	Ward No.	Ward Name
DASARAHALLI	13	Mallasandra
Street ID	**Street Name**	**Significant Landmark**
I0129, W0168, W0121, W0175, W0172	NA	RAVINDRA NAGARA
Segment No.	**Total Length (m)**	
13/C-I0129/S010759	315.80	

Segment Details

Seg No.	Length (m)	Start Coordinates		End Coordinates		From	To
1	106.56	77.518456	13.052596	77.519375	13.052255	3RD MAIN	2ND MAIN
2	209.24	77.517668	13.053251	77.519459	13.052550	2ND MAIN	4TH MAIN

Work Details

History of Road / Lane / Circles

Name of the Work	Sanctioned Estimated Amount (Rs.)	Sanctioned Year
IMPROVEMENTS TO FOOTPATH 8TH ,7TH CROSS ROADS OF 3RD MAIN ROAD	1500000	2014
Year	**Type of Work**	**Other Work Type**
2014 - 2015	Footpath Layering	
Tender	**Work Details**	**Job No. / Work Code**
Tender		013-15-000009
Work Order No.	**Work Order Date**	**Period of Extention**
EE\DD\WO\339\14-15	31/03/2015	
Defect Liability Period From	**Defect Liability Period To**	**Multiple road involved with the same Job No/ Work Code #**
		Yes

Contractor Details

Name of Contractor	Contractor Reg No (BBMP/PWD)	Expenditure Booked \ Released (Rs)
B UMESH		0.00
Phone No.	**E-Mail ID**	
9980485938		

Zone: DASARAHALLI **Ward No:** 13 **Ward Name:** Mallasandra **Street ID:** I0129, W0168, W0121, W0175,

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, [illegible] ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು [illegible] ಪಾಲಿಕೆ
ಎಸ್.ಎಂ ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು

Field Inspection Details

Number of Trees	Any Other Information	Name
0		Nagabhushan G

Date of Inspection	Remarks
15/09/2015	

Category	Image	Photo Remark
Drain Condition		This photo seems out of range
Footpath Condition		This photo seems out of range

Remarks

Designation	Approver Name	Date	Target Date	Remark
CE	SIDDEGOWDA	15/09/2015	15/10/2015	
EE	MALATHESHA R	15/09/2015	15/10/2015	
AEE	JAYALINGAPPA BL	15/09/2015	15/10/2015	
AE	NAGABHUSHAN G	15/09/2015	15/10/2015	
AE	NAGABHUSHAN	15/09/2015	15/10/2015	

Zone: DASARAHALLI **Ward No:** 13 **Ward Name:** Mallasandra **Street ID:** I0129, W0168, W0121, W0175,

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶಿಬ್ಬಹಳ್ಳಿ ಉಪವಿಭಾಗ, ಬಾಸವಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.
